

subject: Chester Springfield Rockingham Windsor STP 2952(1) Construction Update (6/24)

Chester Springfield Rockingham Windsor STP 2952(1) Weekly Construction Update (6/24/2016):

No work will take place on the project from noon Friday the 1st to Tuesday Morning the 5th for the July 4th holiday period.

Springfield:

Ryebrook Construction continued rehabilitation of catch basins, sewer and telephone manholes this week and are scheduled to be finished by the middle of next week. Once structure work is complete, Ryebrook will continue sidewalk tip downs with detectable warning surfaces. (Photos attached)

Windsor:

United Construction continued paving side road aprons on Route 44 and Route 5 as well as driveway aprons on Route 44 and 5. United is scheduled to complete side road and driveway aprons by the middle of next week. L&D Safety Markings followed the paving operation installing durable tape markings. Pike Industries installed aggregate shoulder, RAP on mainline Route 44 and 5 Tuesday and Wednesday and will finish backing up the edge of pavement once paving is complete on side roads and driveway aprons. Nicom Coatings began installation of Asphaltic Plug Joints on Route 44 yesterday. Nicom coatings will return to the project the middle of next week to finish asphaltic plug joints on Route 44 and 5. (Photos attached)

Chester:

No work performed in Chester this week. Punch list items are not complete.

Rockingham:

No work performed in Rockingham this week. Punch list items are not complete.

There will be alternating one-way traffic around construction activities. **We would like to emphasize that there will be access to all businesses along the project routes.**

For more information regarding this project, please see the attached project factsheet and visit our project website: wcrs.vtransprojects.vermont.gov

If you have any questions regarding this project, feel free to contact me directly at 802-324-5522.

Best,
Jacquie

Please focus on safety when driving through the construction work zone and remember, it is against the law to use a hand held cell phone while driving.

Jacqueline Dagesse, MBA, CPESC, PMP
Project Outreach Manager

EIV Technical Services
www.eivtech.com
55 Leroy Rd., Suite 15
Williston, VT 05495
off: 802.497.3653
cell: 802.324.5522
fax: 802.497.3656

Chester, Springfield, Rockingham and Windsor Class I Town Highways US Route 5, VT 44, VT 11 & VT 103

Project work will begin in April 2016 for the towns of Windsor and Springfield. The project will be complete by the end of July 2016.

Contractor: Pike Industries, Inc.

Bid: \$ 9,461,224

Project Manager: Mike Fowler, PE

Regional Engineer: Ann Gammell, PE

Resident Engineer: Ryan Darling

The project work will begin in Springfield on VT 11 in April 2016. The project area will extend along VT 11 for 2.841 miles within the town limits.

The project work in Windsor includes 0.818 miles along US Route 5 and 3.355 miles along VT 44, as shown on the map below.

PROJECT MILESTONES

Contract Award

June 2015

Target Construction Schedule

Rockingham

July 2015 thru June 2016

Chester


August 2015 thru June 2016

Springfield

April 2016 thru July 2016

Windsor

May 2016 thru July 2016

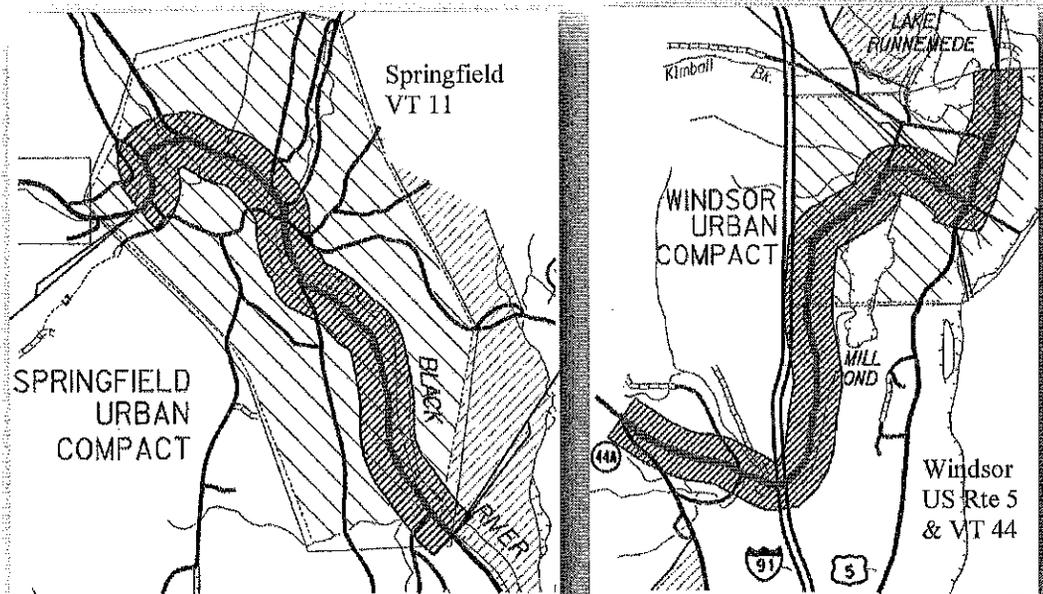

Project work in both Windsor and Springfield includes: cold planning the existing roadway and resurfacing with a leveling course and a wearing course. It also includes: new pavement markings, guardrail, signs, drainage improvements, sidewalk ramps, and other highway related items.

For additional information regarding this project, please contact the Project Outreach Manager, Jacqueline Dagesse at jdagesse@eivtech.com or directly at 802-324-5522.



Chester, Springfield, Rockingham and Windsor Class I Town Highways US Route 5, VT 44, VT 11 & VT 103

Remaining project work in the Towns of Rockingham and Chester will begin in April 2016. Project work in these towns will be complete by June 2016.

Contractor: Pike Industries, Inc.

Bid: \$ 9,461,224

Project Manager: Mike Fowler, PE

Regional Engineer: Ann Gammell, PE

Resident Engineer: Ryan Darling

The project work will begin in Rockingham on US Route 5 on July 29, 2015. The project area along this roadway starts at the town line of Rockingham and Westminster, VT and extends 1.498 miles northerly. Project work in Chester will start in early August 2015, and the project area includes 1.666 miles along VT 103, 0.85 miles along VT 11, and 0.202 miles along Depot Street as shown on the map below.

PROJECT MILESTONES

Contract Award

June 2015

Target Construction Schedule

Rockingham

July 2015 thru June 2016

Chester



August 2015 thru June 2016

Springfield

April 2016 thru July 2016

Windsor

May 2016 thru July 2016

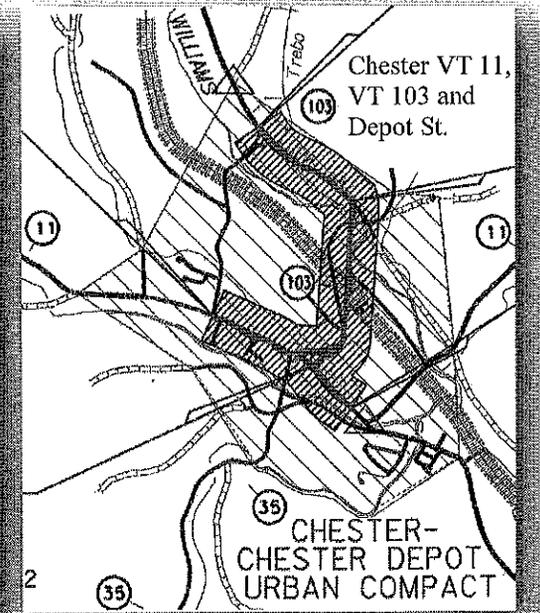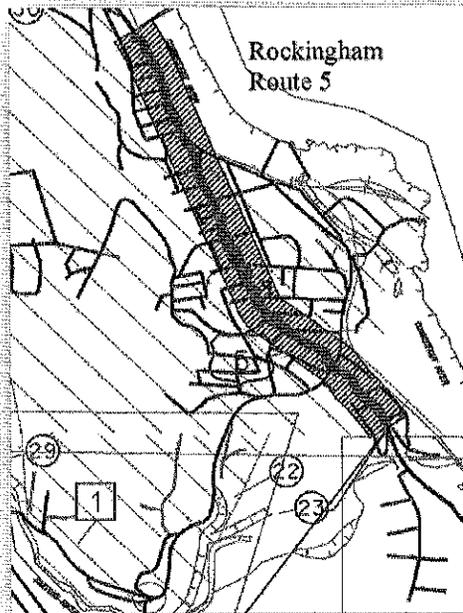

Project work in both Rockingham and Chester includes: cold planning the existing roadway and resurfacing with a leveling course and a wearing course. It also includes: new pavement markings, signs, drainage improvements, sidewalk ramps, and other highway related items. There will be a rail grade crossing rehabilitation in Chester Depot.

For additional information regarding this project, please contact the Project Outreach Manager, Jacqueline Dagesse at jdagesse@eivtech.com or directly at 802-324-5522.



<https://www.facebook.com/pages/VTrans/143848835653728>



<https://twitter.com/511VT>
