

From: Jacqueline Dagesse [mailto:jdagesse@eivtech.com]

Sent: Thursday, July 28, 2016 2:15 PM

To: Jacqueline Dagesse <jdagesse@eivtech.com>

Subject: Chester-Springfield-Rockingham-Windsor STP 2952(1) Weekly Update 7/28/16

Chester Springfield Rockingham Windsor STP 2952(1) Weekly Construction Update (7/28/2016):

Springfield:

Nicom Coatings began plug joint work Monday and are scheduled to be complete by today (photo attached). Tristate Signs poured type B sign foundations at the east end of the intersection of VT 11 and VT 106 yesterday and will be setting posts and hanging signs the beginning of next week. Waters Excavation completed placement of topsoil and seeding around sidewalk tip downs. They also completed thinning and trimming for sight distance of signs. Punch list items are not complete.

Windsor:

Pike performed work on punch list items, including the placement of shoulder backup to select remaining areas. Waters Excavation completed placement of topsoil and seeding around sidewalk tip downs. They also completed thinning and trimming for sight distance of signs. Punch list items are not complete.

Chester:

Tristate Signs poured type B sign foundations at VT 103 and Depot Street yesterday, and they will be setting posts and hanging signs the beginning of next week. Pike performed work on punch list items, including the placement of shoulder backup to select remaining areas. Engineers Construction, Inc. will be setting new solar powered school zone flashing beacons on VT 11 this Tuesday and they will complete the removal of existing beacons by Wednesday. Waters Excavation completed placement of topsoil and seeding around sidewalk tip downs. They also completed thinning and trimming for sight distance of signs. Punch list items are not complete.

Rockingham:

Waters Excavation completed thinning and trimming for sight distance of signs. Punch list items are not complete.

There will be alternating one-way traffic around construction activities. **We would like to emphasize that there will be access to all businesses along the project routes.**

For more information regarding this project, please see the attached project factsheet and visit our project website: wcrs.vtransprojects.vermont.gov

If you have any questions regarding this project, feel free to contact me directly at 802-324-5522.

Best,
Jacquie

Please focus on safety when driving through the construction work zone and remember, it is against the law to use a hand held cell phone while driving.

--

Jacqueline Dagesse, MBA, CPESC, PMP
Project Outreach Manager

EIV Technical Services

www.eivtech.com

55 Leroy Rd., Suite 15

Williston, VT 05495

off: 802.497.3653

cell: 802 324 5522



Chester, Springfield, Rockingham and Windsor Class I Town Highways US Route 5, VT 44, VT 11 & VT 103

Project work will begin in April 2016 for the towns of Windsor and Springfield. The project will be complete by the end of July 2016.

Contractor: Pike Industries, Inc.

Bid: \$ 9,461,224

Project Manager: Mike Fowler, PE

Regional Engineer: Ann Gammell, PE

Resident Engineer: Ryan Darling

The project work will begin in Springfield on VT 11 in April 2016. The project area will extend along VT 11 for 2.841 miles within the town limits.

The project work in Windsor includes 0.818 miles along US Route 5 and 3.355 miles along VT 44, as shown on the map below.

PROJECT MILESTONES

Contract Award

June 2015

Target Construction Schedule

Rockingham

July 2015 thru June 2016

Chester



August 2015 thru June 2016

Springfield

April 2016 thru July 2016


Windsor

May 2016 thru July 2016

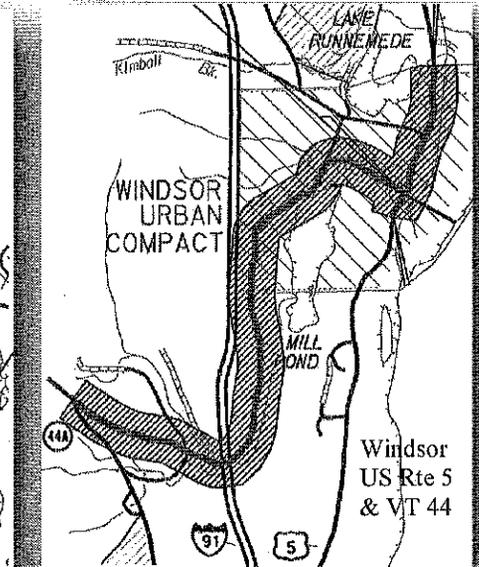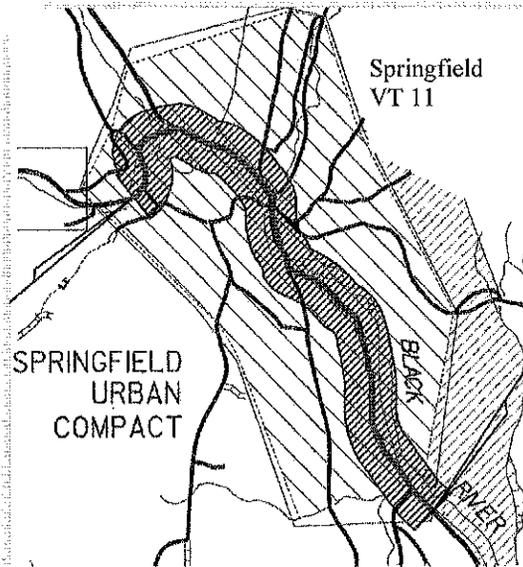

Project work in both Windsor and Springfield includes: cold planning the existing roadway and resurfacing with a leveling course and a wearing course. It also includes: new pavement markings, guardrail, signs, drainage improvements, sidewalk ramps, and other highway related items.

For additional information regarding this project, please contact the Project Outreach Manager, Jacqueline Dagesse at jdagesse@eivtech.com or directly at 802-324-5522.

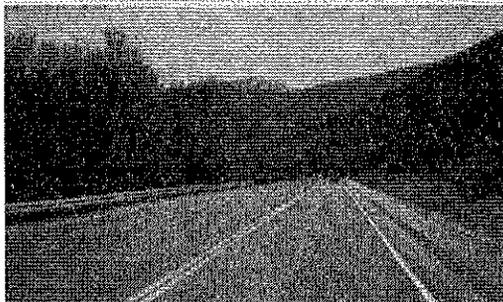

Chester, Springfield, Rockingham and Windsor Class I Town Highways US Route 5, VT 44, VT 11 & VT 103

Remaining project work in the Towns of Rockingham and Chester will begin in April 2016. Project work in these towns will be complete by June 2016.

Contractor: Pike Industries, Inc.

Bid: \$ 9,461,224

Project Manager: Mike Fowler, PE

Regional Engineer: Ann Gammell, PE

Resident Engineer: Ryan Darling

PROJECT MILESTONES

Contract Award

June 2015

Target Construction Schedule

Rockingham

July 2015 thru June 2016

Chester


August 2015 thru June 2016

Springfield

April 2016 thru July 2016

Windsor

May 2016 thru July 2016

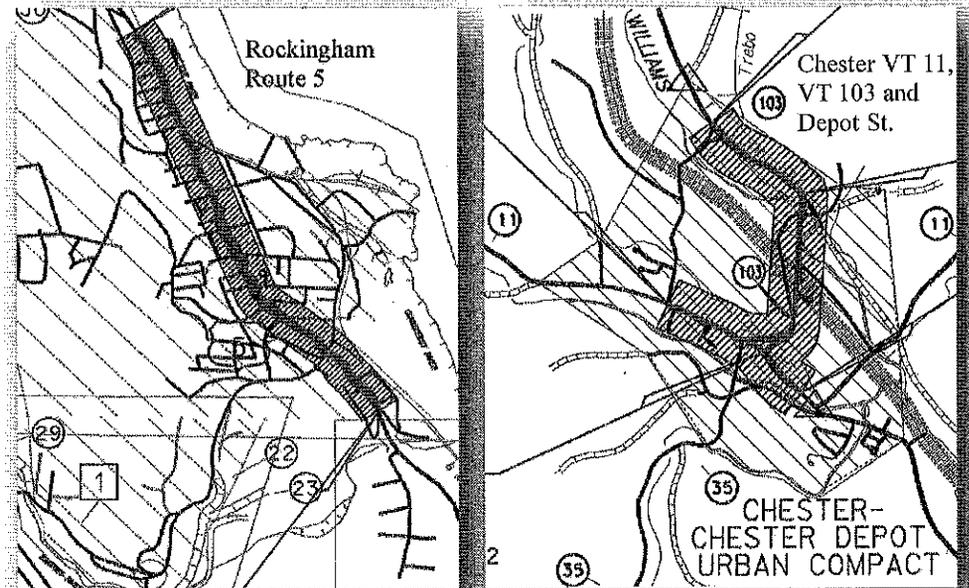

Project work in both Rockingham and Chester includes: cold planning the existing roadway and resurfacing with a leveling course and a wearing course. It also includes: new pavement markings, signs, drainage improvements, sidewalk ramps, and other highway related items. There will be a rail grade crossing rehabilitation in Chester Depot.

For additional information regarding this project, please contact the Project Outreach Manager, Jacqueline Dagesse at jdagesse@eivtech.com or directly at 802-324-5522.



<https://www.facebook.com/pages/VTrans/143848835653728>



<https://twitter.com/511VT>
