

Begin forwarded message:

**From:** Jacqueline Dagesse <[jdagesse@eivtech.com](mailto:jdagesse@eivtech.com)>  
**Date:** July 21, 2016 at 7:19:22 PM EDT  
**To:** Jacqueline Dagesse <[jdagesse@eivtech.com](mailto:jdagesse@eivtech.com)>  
**Subject:** Chester-Springfield-Rockingham-Windsor STP 2952(1) Weekly Update 7/21/16

**Chester Springfield Rockingham Windsor STP 2952(1) Weekly Construction Update (7/21/2016):**

**Springfield:**

Pike Industries and United Construction completed paving of the wearing course this week including driveways and town highway aprons. L&D finished durable tape markings along with the paving operation. Nicom will begin plug joint work mid-next week. Tristate Signs removed two overhead signs at the intersection of VT 11 and VT 106. Tristate Signs will install sign foundations at the east end of the intersection of VT 11 and VT 106 next week.

**Windsor:**

Ryebrook Construction performed work on punch list items, including adjusting the height of a sewer manhole at the West end of VT 44. Punch list items are not complete.

**Chester:**

Tristate Signs will install sign foundations next week at the intersection of VT 103 and Depot Street. Ryebrook Construction performed work on punch list items Tuesday, including replacement of a damaged sidewalk tip down at the intersection of VT 11 and VT 103. Punch list items are not complete.

**Rockingham:**

Pike performed work on punch list items this week. Punch list items are not complete.

There will be alternating one-way traffic around construction activities. **We would like to emphasize that there will be access to all businesses along the project routes.**

1

For more information regarding this project, please see the attached project factsheet and visit our project website: [wcrs.vtransprojects.vermont.gov](http://wcrs.vtransprojects.vermont.gov)


If you have any questions regarding this project, feel free to contact me directly at 802-324-5522.

Best,  
Jacquie

**Please focus on safety when driving through the construction work zone and remember, it is against the law to use a hand held cell phone while driving.**

---  
Jacqueline Dagesse, MBA, CPESC, PMP  
*Project Outreach Manager*

EIV Technical Services



# Chester, Springfield, Rockingham and Windsor Class I Town Highways US Route 5, VT 44, VT 11 & VT 103

**Project work will begin in April 2016 for the towns of Windsor and Springfield. The project will be complete by the end of July 2016.**

**Contractor:** Pike Industries, Inc.

**Bid:** \$ 9,461,224

**Project Manager:** Mike Fowler, PE

**Regional Engineer:** Ann Gammell, PE

**Resident Engineer:** Ryan Darling

The project work will begin in Springfield on VT 11 in April 2016. The project area will extend along VT 11 for 2.841 miles within the town limits.

The project work in Windsor includes 0.818 miles along US Route 5 and 3.355 miles along VT 44, as shown on the map below.

## PROJECT MILESTONES

### *Contract Award*

June 2015

### *Target Construction Schedule*

#### Rockingham

July 2015 thru June 2016

#### Chester


August 2015 thru June 2016

#### Springfield

April 2016 thru July 2016


#### Windsor

May 2016 thru July 2016

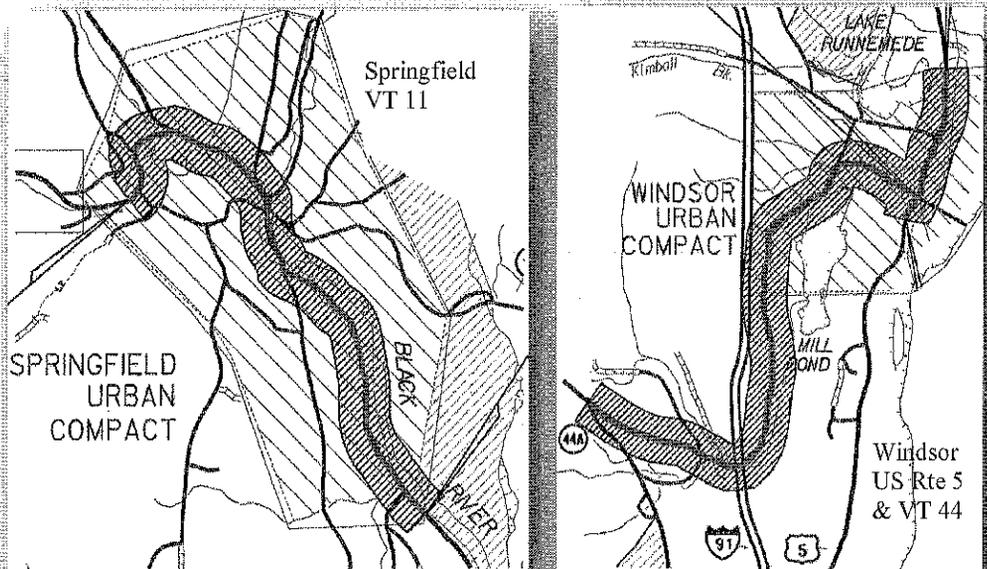

Project work in both Windsor and Springfield includes: cold planning the existing roadway and resurfacing with a leveling course and a wearing course. It also includes: new pavement markings, guardrail, signs, drainage improvements, sidewalk ramps, and other highway related items.

*For additional information regarding this project, please contact the Project Outreach Manager, Jacqueline Dagesse at [jdagesse@eivtech.com](mailto:jdagesse@eivtech.com) or directly at 802-324-5522.*





# Chester, Springfield, Rockingham and Windsor Class I Town Highways US Route 5, VT 44, VT 11 & VT 103

**Remaining project work in the Towns of Rockingham and Chester will begin in April 2016. Project work in these towns will be complete by June 2016.**

**Contractor:** Pike Industries, Inc.

**Bid:** \$ 9,461,224

**Project Manager:** Mike Fowler, PE

**Regional Engineer:** Ann Gammell, PE

**Resident Engineer:** Ryan Darling

## PROJECT MILESTONES

### *Contract Award*

June 2015

### *Target Construction Schedule*

#### **Rockingham**

July 2015 thru June 2016

#### **Chester**

August 2015 thru June 2016


#### **Springfield**

April 2016 thru July 2016

#### **Windsor**

May 2016 thru July 2016

The project work will begin in Rockingham on US Route 5 on July 29, 2015. The project area along this roadway starts at the town line of Rockingham and Westminster, VT and extends 1.498 miles northerly. Project work in Chester will start in early August 2015, and the project area includes 1.666 miles along VT 103, 0.85 miles along VT 11, and 0.202 miles along Depot Street as shown on the map below.

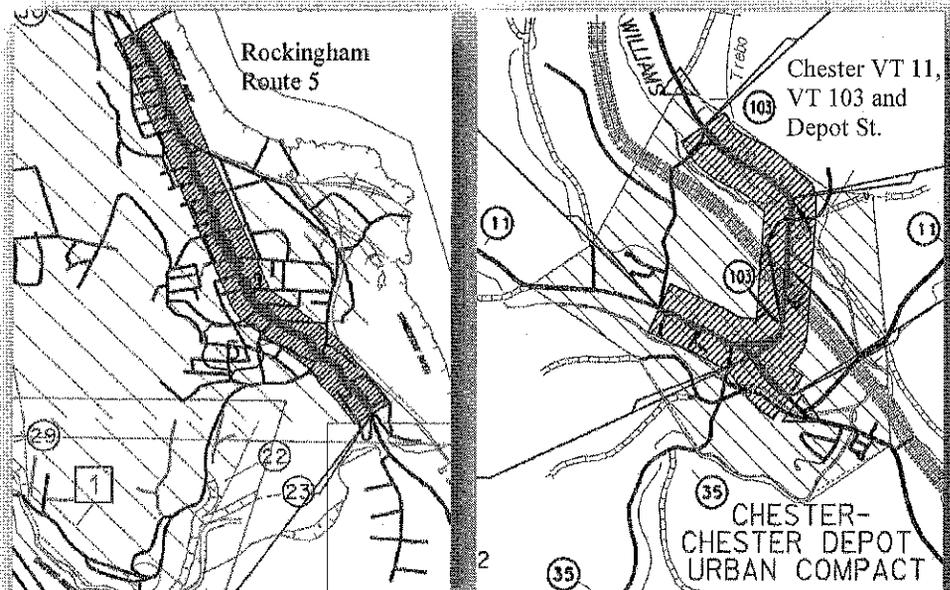

Project work in both Rockingham and Chester includes: cold planning the existing roadway and resurfacing with a leveling course and a wearing course. It also includes: new pavement markings, signs, drainage improvements, sidewalk ramps, and other highway related items. There will be a rail grade crossing rehabilitation in Chester Depot.

*For additional information regarding this project, please contact the Project Outreach Manager, Jacqueline Dagesse at [jdagesse@eivtech.com](mailto:jdagesse@eivtech.com) or directly at 802-324-5522.*



<https://www.facebook.com/pages/VTrans/143848835653728>



<https://twitter.com/511VT>
