

We aren't done yet

From: Jacqueline Dagesse [mailto:jdagesse@eivtech.com]
Sent: Thursday, August 4, 2016 9:22 AM
To: Jacqueline Dagesse <jdagesse@eivtech.com>
Subject: Chester-Springfield-Rockingham-Windsor STP 2952(1) Weekly Update 8/4/16

Chester Springfield Rockingham Windsor STP 2952(1) Weekly Construction Update (8/4/2016):

Springfield:

Pike performed work on punch list items, including paving and backing up edge of pavement on areas that were missed. Tristate Signs completed setting posts and hanging signs this week at the intersection of VT 11 & VT 106. L&D Markings worked on painting items throughout the project. Vermont Rec worked on guardrail and yielding marker post punch list items. ECI completed work on the pedestrian crossing signals at the intersection of VT 11 and McDonalds. Punch list items are not complete.

Windsor:

Pike paved select remaining areas on Route 5 and picked up piles of asphalt. Vermont Rec worked on guardrail and yielding marker post punch list items. Punch list items are not complete.

Chester:

Tristate Signs set posts and hung signs at VT 103 and Depot St this week. Pike performed work on punch list items, including placing shoulder backup to select areas. Engineers Construction, Inc. set new solar powered school zone flashing beacons on VT 11 this past Tuesday and Wednesday. Engineers Construction, Inc. will remove existing beacons next week. Waters Excavation will be onsite next week to re-seed select areas around the railroad crossing to ensure desired turf establishment is achieved. L&D Markings will continue repainting damaged markings. Punch list items are not complete.

Rockingham:


L&D Markings will continue working on punch list painting items and repairing damaged markings. Punch list items are not complete.

There will be alternating one-way traffic around construction activities. **We would like to emphasize that there will be access to all businesses along the project routes.**

For more information regarding this project, please see the attached project factsheet and visit our project website: wcrs.vtransprojects.vermont.gov

If you have any questions regarding this project, feel free to contact me directly at 802-324-5522.

Chester, Springfield, Rockingham and Windsor Class I Town Highways US Route 5, VT 44, VT 11 & VT 103



Remaining project work in the Towns of Rockingham and Chester will begin in April 2016. Project work in these towns will be complete by June 2016.

Contractor: Pike Industries, Inc.

Bid: \$9,461,224

Project Manager: Mike Fowler, PE

Regional Engineer: Ann Gammell, PE

Resident Engineer: Ryan Darling

PROJECT MILESTONES

Contract Award

June 2015

Target Construction Schedule

Rockingham

July 2015 thru June 2016

Chester

August 2015 thru June 2016


Springfield

April 2016 thru July 2016

Windsor

May 2016 thru July 2016

The project work will begin in Rockingham on US Route 5 on July 29, 2015. The project area along this roadway starts at the town line of Rockingham and Westminster, VT and extends 1.498 miles northerly. Project work in Chester will start in early August 2015, and the project area includes 1.666 miles along VT 103, 0.85 miles along VT 11, and 0.202 miles along Depot Street as shown on the map below.

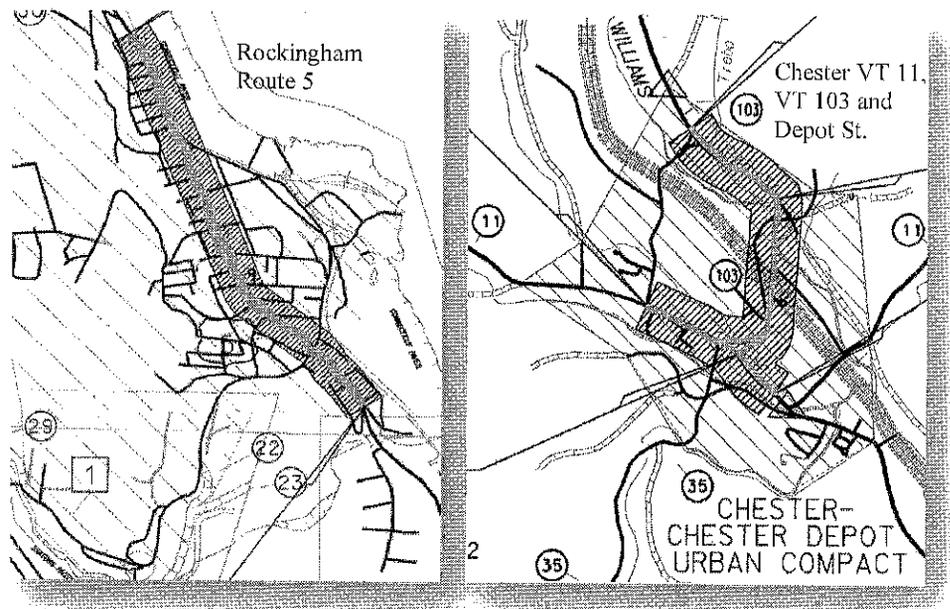

Project work in both Rockingham and Chester includes: cold planning the existing roadway and resurfacing with a leveling course and a wearing course. It also includes: new pavement markings, signs, drainage improvements, sidewalk ramps, and other highway related items. There will be a rail grade crossing rehabilitation in Chester Depot.

For additional information regarding this project, please contact the Project Outreach Manager, Jacqueline Dagesse at jdagesse@eivtech.com or directly at 802-324-5522.



<https://www.facebook.com/pages/VTrans/143848835653728>



<https://twitter.com/511VT>

Chester, Springfield, Rockingham and Windsor Class I Town Highways US Route 5, VT 44, VT 11 & VT 103

Project work will begin in April 2016 for the towns of Windsor and Springfield. The project will be complete by the end of July 2016.

Contractor: Pike Industries, Inc.

Bid: \$ 9,461,224

Project Manager: Mike Fowler, PE

Regional Engineer: Ann Gammell, PE

Resident Engineer: Ryan Darling

The project work will begin in Springfield on VT 11 in April 2016. The project area will extend along VT 11 for 2.841 miles within the town limits.

The project work in Windsor includes 0.818 miles along US Route 5 and 3.355 miles along VT 44, as shown on the map below.

PROJECT MILESTONES

Contract Award

June 2015

Target Construction Schedule

Rockingham

July 2015 thru June 2016

Chester


August 2015 thru June 2016

Springfield

April 2016 thru July 2016

Windsor

May 2016 thru July 2016

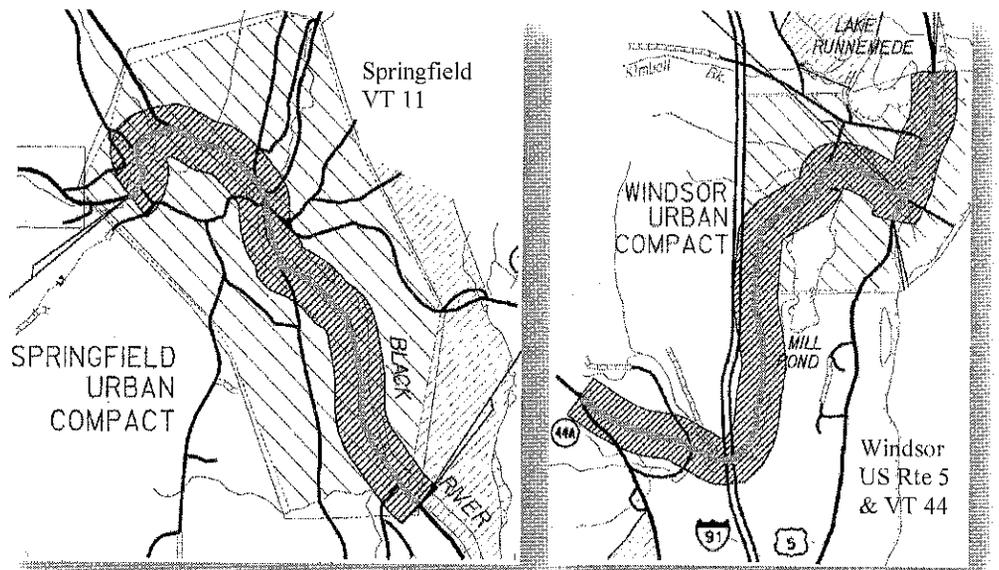

Project work in both Windsor and Springfield includes: cold planning the existing roadway and resurfacing with a leveling course and a wearing course. It also includes: new pavement markings, guardrail, signs, drainage improvements, sidewalk ramps, and other highway related items.

For additional information regarding this project, please contact the Project Outreach Manager, Jacqueline Dagesse at jdagesse@eivtech.com or directly at 802-324-5522.

